



THE CORPORATION OF THE TOWNSHIP OF NORTH STORMONT
REQUEST FOR QUOTATION
FOR
Salt Shed
(Fabric Membrane Structure)
RFQ-PW-003-2021

CLOSING

DATE: Friday April 23rd, 2021
TIME: 12:00 P.M. (NOON)
LOCATION: TOWNSHIP OF NORTH STORMONT
15 Union Street, Berwick, ON
Phone: 613-984-2821
LATE QUOTATIONS WILL NOT BE ACCEPTED

The Corporation of the Township of North Stormont reserves the right to accept or reject all or part of any Quotation and also reserves the right to accept other than the lowest Quotation and to cancel this Request for Quotation at any time.

The Corporation of the Township of North Stormont
RFQ-PW-003-2021
Salt Shed (Fabric Membrane Structure)
Closing Date: April 23rd, 2021

SCOPE OF WORK AND SPECIFICATION

PART 1

1.1 INTENT OF SPECIFICATION

- 1.1.1 This specification covers the design, manufacture, shipping, handling and erection of a prefabricated membrane covered structure.
- 1.1.2 The specification as heretofore set forth is general in nature and scope and shall not be construed as to limit the work other than the requirement that the new re-locatable building shall match the specification in materials, appearance, configuration and details.
- 1.1.3 It is the intent of this specification that the bidder shall include all labor, materials, equipment services and transportation to locate the building on the site designated with all other work.
- 1.1.4 Buildings shall be complete and operating and shall include all exterior and interior materials and systems as shown or indicated in contract documents.
- 1.1.5 All workmen shall be skilled and qualified for the work that they perform. All materials used, unless otherwise specified, shall be new and of the types and grades specified. The contractor shall certify that no asbestos containing building materials that exceed Federal mandated safe asbestos levels have been used in the construction of the membrane-covered structure.
- 1.1.6 Work shall be performed as necessary and required for the construction of the project as indicated. Such work includes the supply and installation of a membrane-covered structure complete with exterior and interior finishes. The building shall be as dimensioned with all features and quantities as per specification.

1.2 APPROVAL OF PLANS

- 1.2.1 **Upon award of this contract, The Contractor shall furnish detailed drawings for all structural work stamped by an engineer certified by the Province of Ontario to verify compliance to local building code. Site specific calculation packages will be provided upon request of the customer (Additional Fees will apply).**
- 1.2.2 All work to be performed under the conditions of this specification shall comply with the rules and regulations of all agencies having jurisdiction for this classification of construction and design and shall conform to the applicable live loads due to wind, rain and snow.
- 1.2.3 Building supplier must provide written certification that they have been in the steel tension membrane building business for 10 years or more under the same name.
- 1.2.4 Duration of the Building supplier warranty must not exceed their number of years of business under the same name.
- 1.2.5 Building supplier must provide written references with contact information for at least three (3) salt sheds currently in operation.

1.3 WORKMANSHIP

- 1.3.1** The workmanship of all materials and components of the structure shall be commensurate with the functional requirements of the item.
- 1.3.2** Building prefabrication shall be performed under factory conditions in a plant specifically arranged for this type of work. Contractor shall provide adequate space, equipment, personnel, and technical ability to coordinate the assembly and factory prefabrication of all major components of the work and all necessary operations in the packing, shipping and installation procedures. No fabrication shall be done until the materials have been tested and approved.
- 1.3.3** Welding: Welding shall be employed only when specified in the original design. Welding shall be in accordance with CSA W47 and CSA W59. The building fabricator must be a CWB approved fabricator. Successful bidder must supply CWB certificate.
- 1.3.4** On Site Welding: If required, on site welding shall completed by CWB certified personnel for the processes and positions employed.
- 1.3.5** Manufacturer: The structure supplier shall be a reputable manufacturer, that shall have at least 10 years direct experience in the design, manufacture and installation of structures of the type specified herein; shall operate according to a comprehensive quality system and shall provide three references with structures in use for at least five years which are clear span and each must enclose an area in excess of the square footage as stated in section 1.2.4.
- 1.3.6** Manufacture must comply with the following:
- a) Certificate to CAN/CSA A660 Certification of Manufactures of Steel Building
 - b) Design and Manufacturing to CAN/CSA S367 Air, Cable and Frame Supported Membrane Structures.
 - c) BMEC authorization

1.4 DIMENSIONS

**THE STRUCTURE SHALL OCCUPY AN AREA OF minimum 8,000 Sq.Ft
100 Ft. Long by 80 ft. Wide**

1.5 SCOPE OF WORK

- 1.5.1** Rigid steel frame supporting membrane covered roof and wall structure of the type described herein:
- a. **The structure must provide a minimum 8' - 10' straight side wall above the foundation. (BUILDING PROFILE BELOW)**
 - b. **Overhead door (specs below)**
 - c. **Personnel door (specs below)**
 - d. Flat gable ends with (2) 4' x 4' passive vents on each end.
 - e. Soffit vent system at top of foundation wall.
 - f. Termination of Fabric to Concrete Wall System

- 1.5.2 Foundation / Wall System and Anchors (Engineered by others 6ft concrete walls)
- 1.5.3 Site Work (by others)
- 1.5.4 Delivery to Site
- 1.5.5 Complete Structure & Accessory Installation

Overhead Door

- Door size to 20'W x 16'H
- Insulated door panels 1 ¾" thick
- 3" Heavy Duty tracks
- Hot Dipped Galvanized springs
- Stainless steel cables
- Rubber rollers with stainless steel shafts
- Electrical operator complete modification for corrosion resistance.

Personnel Door

- 36" wide code compliant steel personnel door
- Complete with panic bar, closer, lock set and latch assembly

PART 2

2.1 GENERAL DESIGN REQUIREMENTS

2.1.1 Scope

1. The membrane shall be tensioned over the framework. The structure shall be rectangular in shape with vertical gable end walls. The interior of the structure below the main trusses shall be clear span free of any structural support members and shall provide unobstructed floor space. No exterior purlins, guy ropes or cables shall be used for anchoring the structure.
2. The structure shall include accessories to the extent shown on the project drawings required for the scope and intended use for:
 - a. Overhead doorways
 - b. Ventilation systems.
 - c. Other structure accessories

2.1.2 Design Requirements - Structural Frame

1. Roof and Wall Surfaces: To provide for maximum compatibility with standard door, window, ventilation and other accessory and cladding systems, the structure shall be designed such that gable surfaces form flat planes.

2. Purlin Spacing: To provide for structural stability and to provide for installation of accessory items, the main structural trusses shall be laterally braced by load bearing purlins at intervals required by the truss design.
3. Wind and Frame Bracing: The structure shall be appropriately stabilized with wind bracing cable as well as any required secondary node restraint assemblies so as to efficiently transfer wind, snow and seismic induced stresses to the foundation/anchoring system. Cable diameter for main wind bracing shall be a minimum of 3/16" diameter and larger if so required. The end bays of the structure shall be designed to be X - braced early during installation to allow for permanent stability of the frame during installation.
4. Connecting Joints: Connections between structural elements shall be designed so as to transfer the compressive and tensile forces present in a given joint. A minimum of Grade 5 bolts shall be used at each truss chord joint. Primary axial steel, secondary purlins, and end wall frame connections shall be made with a minimum of Grade 5 hex bolts, carriage bolts and self drilling screws.
5. Mechanical Equipment Interface: The main structural roof trusses shall allow for installation of electrical and mechanical equipment based on collateral loads as defined in section 2.2.2. Likewise, the structure shall accept penetrations through the membrane for access doors and mechanical services with minimal modification.
6. Shipping: The main structural trusses shall be standard planar-style trusses which nest tightly together in order to minimize shipping and storage volume.

2.1.3 Design Requirements - Membrane Cladding System

1. Membrane: The roof membrane shall form a weather tight shell over the structural frame. In order to provide for a good finished appearance and to ensure weather tightness, the membrane shall be assembled and tensioned, in a manner to minimize wrinkles in hot and cold temperatures.
2. The gable wall membrane cladding shall be manufactured and connected to form one piece to the adjacent end wall and roof cladding.
3. Roof membrane longitudinal stretch shall be maintained with 1" ratchets ILO lacing rope. Circumferential stretch shall be maintained with a winch lock system requiring minimal ongoing maintenance.
4. Base Tensioning System: The membrane cladding will be provided with a mechanical tensioning system that allows the membrane to be fully tensioned around the structure perimeter. The system will be designed such that the membrane can be tightly and neatly secured over the structural frame and such that the system has remaining range of adjustment.
5. Membrane Seal at Openings and Base: The Dealer supplying the structure will provide all materials and methods necessary to fully tension and seal the membrane material around all door, ventilation and other openings as well as around the structure perimeter below the main tensioning system. This seal shall provide a neat and finished appearance and eliminate any loose membrane cladding that could otherwise be damaged by flapping or abrasion.

6. The membrane shall not be designed to function as a structural member such that, should any damage to or penetrations of the membrane occur, the integrity of the structural framework shall not be affected.
7. The Contractor shall provide drawings and calculations acceptable to the Architect/Engineer of Record, meeting the provisions of the applicable Building Code. The Contractor shall bear all costs for production of drawings and associated structural calculations. Contractor shall make all revisions and corrections to those documents required for approval and shall resubmit as required to obtain approvals.
8. Successful bidders shall make all required changes or corrections and will deliver to the Owner's Architect all approved drawings and reactions.

2.2 ENGINEERED DESIGN CRITERIA

- 2.2.1 The structure shall be designed using methodology as per the applicable building code. Structural members shall be designed using according to CSA S16. Appropriate safety factors to yield and ultimate shall be maintained. An appropriately justified analysis method which considers both the large displacement geometric and material nonlinearities of the fabric cladding shall be used in determination of the load effects on all supporting elements. Upon request, use of the methodology must proven by providing a detailed calculation package. The use of Metal Building Software (MBS) is not acceptable for the aforementioned analysis.
- 2.2.2 Importance Category: **Low**
- 2.2.3 Snow / Rain Loads: The structure shall be designed based upon a minimum ground snow load of **2.2** Kilopascal (kPa) and **0.4** kPa of rain load. At a minimum, the structure shall be capable of supporting a roof a collateral load of **0.012** kPa over the entire roof area or portion of the roof area, and any probable arrangement of loading resulting in the highest stress in the members, or as prescribed by the applicable building code.
- 2.2.4 Wind Loads: The structure shall be capable of withstanding a basic 1/50 wind pressure of **0.41** kPa.
- 2.2.5 Deflection: For safety of specified or future suspended accessories, the maximum allowable deflection of structural members shall be no more than 1/180 of the clear span of that member when subjected to the design loads described herein.
- 2.2.6 Design Loads: The design shall be based as a minimum on the design loads and combinations specified in the applicable building code.

2.3 OPERATION AND USE

- 2.3.1 The main structural frame and cover shall be warranted to provide a minimum 15-year operational use period with appropriate inspection and maintenance.
- 2.3.2 The structure shall be capable of being assembled, operated, and dismantled in all ambient

temperatures between -20°F and 120°F.

2.4 MATERIALS

2.4.1 All materials used in the structure shall be new, without defects and free of repairs. The quality of the materials used shall be such that the structure is in conformance with the performance requirements as specified herein.

2.4.2 Cladding Membrane: The structure shall be clad with an **FRU coated polyolefin fabric** manufactured by an approved and reputable supplier with demonstrated long-term performance. The polyolefin membrane fabric shall be waterproof and free from defects. All roofs, walls, end walls and connecting sections shall be weather tight. The material will be selected from the manufacturer's standard colors for the sidewalls and roof panels. The material scrim and coating must be UV stabilized, **fire retardant, and must carry a minimum fifteen-year manufacturer's warranty and have a minimum life expectancy of 15 to 20 years. The minimum fabric specification is as follows:**

| | |
|----------------------------|--|
| Total Fabric Weight | 12.0 oz/yd ² (407 g/m ²) +/- 5% |
| Coating Thickness | 4 mils average, each side |
| Finished Thickness | 22 mils (ASTM D-5199) |
| Grab Tensile Strength | 370 lbs (ASTM D-751) |
| Strip tensile Strength | 250 lbs/in (ASTM D-751) |
| Tongue Tear Strength | 110 lbs (ASTM D-2261) |
| Trapezoidal Tear | 100 lbs (ASTM D-4533) |
| Mullen Burst | 650 psi (ASTM D-3786) |
| Cold Crack Resistance | -60 °C (ASTM D-2136) |
| UV Resistance & Weathering | 90% retention after 2000 hr.(ASTM G151) |
| Flame Spread | 5 or less (ASTM E84) |
| Smoke Developed | 58 or less (ASTM E84) |
| Flame Resistance | 2 sec flame (NFPA 701) |

Acceptable membrane suppliers include: Fabrene, Intertape and Hagihara. The membrane manufacturer must demonstrate a minimum of **five** years successful field experience with provision of polyolefin membrane cladding in use on similar or larger size structures of the type contemplated in this specification.

2.4.3 Metal: The main structure shall consist of a welded truss arches with parallel tube chords separated apart by webbing. A minimum of 3" of weld shall join the web to the cord at each location. The web shall be an open section to allow access to all surface areas for hot dip galvanization. Continuous tubular webbing is not acceptable.

2.4.4 Truss sections are manufactured and post dip galvanized to ensure proper protection on the inside as well as the external surfaces of the truss sections. **All sections must be hot dip galvanized post fabrication to a minimum of CSA G-164 / ASTM A123-15.** Truss will be manufactured of a cold-formed and induction welded modified grade carbon steel, providing a finished tubular product with exceptional mechanical and corrosion resistant properties.

2.4.5 Tolerances: All dimensional tubing tolerances are in accordance with ASTM A500, Section 10.

- 2.4.6** Tubing shall be manufactured using steel conforming to ASTM A568, ASTM A1011 and G40.21 350W. Finished steel tubing used in the structure must have minimum structural and mechanical properties based on standard ASTM A500.
- 2.4.7** All steel flat bar, cross rods and other steel components shall be fabricated from hot dipped galvanized material, meet the stated standards and have minimum structural and mechanical properties based on standard CSA G40.20/40.21-44W or ASTM A572 Grade C
- 2.4.8** Corrosion Protection: as per 2.4.4 all Metal sections shall be hot dipped galvanized to a minimum of CSA G-164 / ASTM A123-15. This allows for maximum protection on **all welded surfaces including the interior sections.**
- 2.4.9** Hardware:
1. Bolts: Bolts subject to extreme stress and wear shall be minimum Grade 5 and shall be hot dip galvanized. All bolts shall be installed per the manufacturers instructions.
 2. Membrane Tensioning Hardware: The fabric membrane shall be tensioned with load rated hardware which is plated/hot dip galvanized so as to prevent corrosion. Hardware shall allow full and free rotation at the foundation connection to avoid fatigue failure of threaded assemblies.
 3. Membrane Tensioning Webbing: The membrane shall be tensioned with load-tested tie-downs.
 4. Cable Assemblies: Main and wind bracing cable assemblies shall be manufactured to the required length and press swaged with metal sleeves. The cables are manufactured using preformed 7-19 stainless steel cables, sized with appropriate safety factors.

| | | |
|------------|---|-------------|
| 3/16" dia. | = | 4,200 lbs. |
| 1/4" dia. | = | 7,000 lbs. |
| 5/16" dia. | = | 9,800 lbs. |
| 3/8" dia. | = | 14,400 lbs. |
| 1/2" dia. | = | 22,800 lbs |
 5. Other Fasteners: Non-structural fasteners such as wood screws, Tek screws, etc., shall be of standard commercial quality
 6. Exterior Trim: The aluminum alloy used in the extrusion shall meet or exceed 6063-T6.
- 2.4.10** Piece marking and Identification: All individual parts or bundles and packages of identical parts are to be clearly marked for identification. Bolts, nuts, washers and fasteners shall be packaged according to type, size and length. Shipping documentation shall include a list showing the description, quantity and piece mark of the various parts, components and elements.
- 2.4.11** Material Delivery: The building system materials shall be delivered to the project site during normal working hours on weekdays. Installation contractor will provide adequate workmen and equipment to promptly unload, inspect and accept material delivery.
- 2.4.12** Handling: The installation contractor shall be responsible for unloading, field storage, protection and transfer to the work area of all materials and equipment required to perform the work. At no time shall materials be dropped, thrown or dragged over the transport equipment or the ground. Damage to any piece under its own or superimposed weight shall be cause for repair or replacement.

- 2.4.13** Short, Damaged or Excess Materials: Installation contractor shall inspect, count and verify quantities based on the shipping documents.

PART 3

3.1 REFERENCES AND STANDARDS

- 3.1.1** The standards listed below are referred to within the document by basic letter designation only. Standards refer to the current approved edition unless noted otherwise. They form a part of this specification to the extent referenced thereto:
- a. American Society for Testing and Materials (ASTM):

| | |
|--------|--|
| A 36 | Structural Steel |
| A 123 | Standard Specification for Zinc (Hot Dip Galvanized) Coatings on Iron and Steel Products |
| F 3125 | Standard Specification for High Strength Structural Bolts and Assemblies |
| A 500 | Standard Specification for Cold Formed Welded And Seamless Carbon Steel Structural Tubing in Rounds and Shapes |
| A 563 | Carbon and Alloy Steel Nuts |
| F 1554 | Standard Specification for Anchor Bolts |
 - b. American Society of Civil Engineers (ASCE) 7 - Minimum Design Loads for Building and Other Structures. Latest edition as required Building Code.
 - c. American Welding Society (AWS)

| | |
|------|---|
| D1.1 | Structural Welding Code-Steel |
| D1.3 | Structural Welding Code-steel sheet steel |
 - d. National Fire Protection Association

| | |
|----------|--|
| NFPA 701 | Standard methods of Fire Tests for Flame Resistant Textiles and Films. |
|----------|--|
 - e. Canadian Standards Associations

| | |
|------------------|--|
| CSA W59 | Welded Steel Construction |
| CSA G40.20/40.21 | General requirements for rolled or welded structural quality steel/Structural quality steel. |
| CSA W47.1 | Fusion Welding Of Steel Company Certification |
| CSA S16 | Design of steel structures |
 - o f) CAN/CSA-G164-M92 or equivalent
 - Current BMEC authorization
 - Current CSA A660 certification

Project Contact

For any questions, comments, clarifications or concerns regarding this RFQ, please contact:

Blake Henderson


Public Works Superintendent

15 Union St. Berwick Ont.

Email: bhenderson@northstormont.ca

Cell: [613-551-0498](tel:613-551-0498)

Phone: [613-984-2821](tel:613-984-2821) ext.227

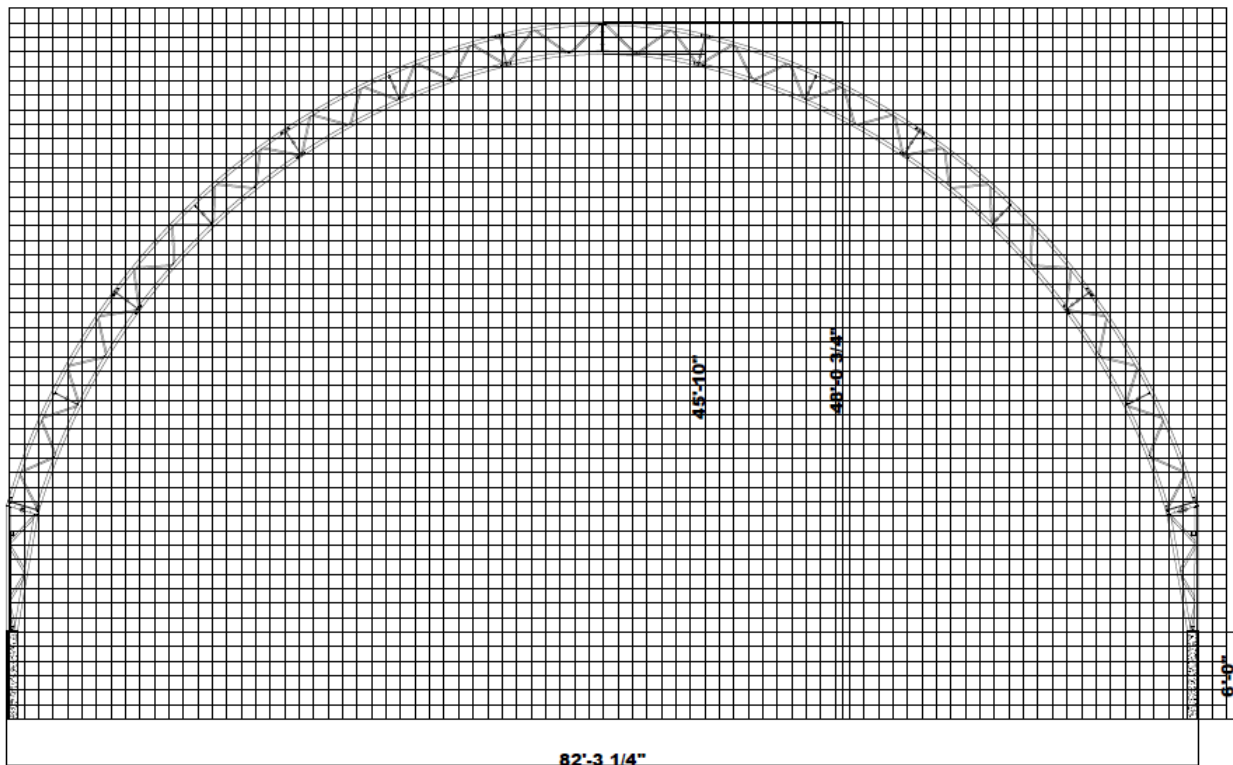

*The Corporation of the Township of North Stormont
RFQ-PW-003-2021
Salt Shed (Fabric Membrane Structure)
Closing Date: April 23rd, 2021*

Part 4 – Form of Quotation

| SUB TOTAL | HST | TOTAL |
|-----------|----------|----------|
| \$ _____ | \$ _____ | \$ _____ |

Company Name: _____

Contact: _____

Address: _____

Phone: _____ **Fax:** _____

Email: _____

HST Number: _____ **WSIB Number:** _____

Date

Signature of Authorized Person (print)

Name of Authorized Person
